

**CHANGE ORDER & AMENDMENT POLICY**  
University of Illinois Office of Capital Programs and Real Estate Services  
January 2025

**I. Governance of University of Illinois Capital Projects**

The majority of capital projects undertaken by the University of Illinois are subject to the requirements of the Illinois Procurement Code (30 ILCS 500). The Board of Trustees of the University of Illinois is a Construction Agency pursuant to the Code. The Board of Trustees and University Administration, through the University Office of Capital Programs and Real Estate Services, establish policies, procedures, systems and other considerations related to capital projects.

This Policy governs expenditures in excess of a capital contract's original price and was developed by the University Office of Capital Programs and Real Estate Services in conjunction with the Office of University Counsel.

**II. Change Orders and Amendments Pursuant to the Illinois Procurement Code**

After a contract has been formed pursuant to the Procurement Code, Section 30-35 of the Code (30 ILCS 500/30-35) permits expenditures in excess of the original contract price provided that the additional work to be performed or material to be furnished: (1) is germane to the original contract; and (2) the expenditure for work is approved in writing by the appropriate authority level prior to the performance of the work or procurement of material. Additional expenditures generally take the form of "Change Orders" in the case of construction contracts and "Amendments" in the case of Professional Services Agreements.

The Procurement Code, procurement rules, University policies, and Contract Documents seek to expedite the process contemplated in Section 30-35 by allowing flexibility to utilize methodologies such as "time and materials" or hourly rates, while requiring the maintenance of adequate cost-control mechanisms. University policies and procedures must be followed to ensure that the proposals underlying the anticipated increased expenditures are appropriate, accurate and cost efficient. University personnel shall negotiate the best possible price for the University when seeking expenditures in excess of the original contract price. Prior written approval by appropriate authority in accordance with this policy must be obtained prior to the obligation of any additional funds.

Should an 'emergency purchase' be required which is not germane to an existing project construction contract, Procurement Code Section 20-30 (30 ILCS 500/20-30) shall be applicable. An 'emergency purchase' pursuant to this section shall be utilized only in instances of a threat to public health or safety, or when immediate expenditure is necessary for repairs to property in order to protect against further loss of or damage to property or the integrity of vital records, or serious disruption of essential services. Issuance of an 'emergency purchase' is entirely within the discretion of the Owner. Prior written approval by appropriate University administrators in accordance with this policy must be obtained prior to the obligation of any funds.

### **III. Definition of Terms, Routing for Approval, & Signature Authorization**

In order to comply with the requirements of the Procurement Code, the University has established Contract Documents, including General Conditions, and utilizes the following definitions, rules and procedures:

#### **A. Change Orders**

“Change Order” means a written order to a Contractor executed by the Owner in accordance with an existing project construction contract authorizing and directing an addition to, deletion from, or adjustment or revision of the requirements of the Contract Documents, or an adjustment to the compensation payable to Contractor, or to the time for performance of the contract and completion of the Project, or a combination thereof. All additional expenditures related to work performed or material purchased through an agreement with a Contractor will ultimately take the form of a Change Order. Change Orders shall utilize the approved format identified by the Office of University Counsel and University Office of Capital Programs and Real Estate Services. In order to comply with Section 30-35 of the Procurement Code, directives of the Board of Trustees, this Policy and other University and campus policies, all Change Orders shall be subject to approval by the appropriate.

#### **1. Field Directive (FD) Definition for Construction**

“Field Directive” means a written order to a Contractor executed by the Owner in accordance with the existing project construction contract authorizing and directing an addition to, deletion from, or adjustment or revision to the requirements of the Contract Documents, or an adjustment to the compensation payable to Contractor, or to the time for performance of the contract and completion of the Project, or a combination thereof. Field Directives may only be utilized in distinct and exceptional situations when, due to circumstances beyond the University’s control, a proposed Change Order is in dispute or the contemplated time of completion for the normal Change Order process would delay the project. Prior to commencement of work, the University shall set forth on the appropriate form “not-to-exceed” costs, which may be lump sum or time and material based, for the contemplated expenditure. A Field Directive is preliminarily authorized/supported with appropriate documentation (see Exhibit 1) and ultimately utilizes the Change Order form. Additional documentation supporting and justifying the completed work shall be required. Field Directives are subject to approval by the appropriate authority. Field directives must have appropriate University approval prior to commencement of the work. Field Directives in excess of the Small Purchase Threshold shall also be approved by the Chief Procurement Office and the Procurement Policy Board prior to the commencement of work.

#### **2. Emergency Work Authorization (EWA) Definition**

“Emergency Work Authorization” means a written order to a Contractor executed by the Owner in accordance with an existing project construction contract and directing an adjustment to the Contract Document requirements according to 30 ILCS 500/20-30. An Emergency Work Authorization shall be utilized only in instances of a threat to public health or safety, loss of or damage to property or the integrity of vital records, or serious disruption of essential services. Issuance of an Emergency Work Authorization is entirely within the discretion of the Owner. Prior to commencement of work, the University shall set forth on the appropriate form “not-to-exceed” time and material costs for the contemplated expenditure. The time of the emergency work shall be limited to no more than 90 days. The time may be extended beyond 90 days with approval by the CPO after a public hearing is published on the Illinois Procurement Bulletin. An Emergency Work Authorization is preliminarily authorized/supported with appropriate documentation (see Exhibit 1) and ultimately utilizes the Change Order form. Prior to commencement of work, an Emergency Work Authorization shall be approved by the appropriate authority. Notice of emergency work shall be provided to the Procurement Policy Board no later than 5 calendar days after the emergency contract is awarded. When the actual final cost is determined, the cost shall also be provided to the Procurement Policy Board prior to the 10<sup>th</sup> day of the succeeding month.

**B. Professional Services Consultant Agreement Amendments**

“Amendment” means a written modification to a Professional Services Agreement and may authorize and direct an addition to, deletion from, or adjustment or revision of the requirements of the Agreement, or an adjustment to the compensation payable to Consultant, or to the time for performance of the contract and completion of the Project, or a combination thereof. Amendments to Professional Service Agreements shall utilize the approved format identified by the Office of University Counsel and University Office of Capital Programs and Real Estate Services. All Professional Services Agreement Amendments shall be approved by the Office of University Counsel and the University Office of Capital Programs and Real Estate Services. Prior written approval by appropriate authority must be obtained prior to the obligation of any additional funds. Amendments in excess of the Small Purchase Threshold shall be approved by the Chief Procurement Office and the Procurement Policy Board prior to commencement of the work.

**1. Field Directive (FD) Definition for Professional Services Consultant (PSC)**

“Field Directive” means a written order to a PSC executed by the Owner in accordance with the existing project construction contract authorizing and directing an addition to, deletion from, or adjustment or revision to the requirements of the Contract Documents, or an adjustment to the compensation payable to PSC, or to the time for performance of the

contract and completion of the Project, or a combination thereof. Field Directives may only be utilized in distinct and exceptional situations when, due to circumstances beyond the University's control, a proposed Amendment is in dispute or the contemplated time of completion for the normal Amendment process would delay the project. PSC Field Directives during design phases should only be generated if the work is considered to be on a critical path of meeting the design phase schedule and cannot be recovered through other methods. Prior to commencement of work, the University shall set forth on the appropriate form "not-to-exceed" costs, which may be lump sum or time and material based, for the contemplated expenditure. A Field Directive is preliminarily authorized/supported with appropriate documentation (see Exhibit 1) and ultimately utilizes the Amendment form. Additional documentation supporting and justifying the completed work shall be required. Field Directives are subject to approval by the appropriate authority. Field directives must have appropriate University approval prior to commencement of the work. Field Directives in excess of the Small Purchase Threshold shall also be approved by the Chief Procurement Office and the Procurement Policy Board prior to the commencement of work.

#### **IV. Signature Authority**

Approval delegated signature authority are established by the University of Illinois Board of Trustees and the University. Amendments and Change Orders that are cumulatively in excess of 5% of the original contract for non-medical center projects and 25% for medical center projects must be reported to the Board of Trustees through the University Office of Capital Programs and Real Estate Services.

#### **V. Amendment Process for Approval**

##### **A. Documentation required**

1. Project name and number
2. Professional Services Consultant's (PSC) name
3. Proposed amendment number
4. Proposed change in scope and rationale for the change including backup documentation
5. Compensation changes submitted in contract format
6. Proposed changes to relevant PSA scope sections
7. Anticipated start date of added scope

##### **B. Approval**

1. The CCU PM shall obtain the PSC's signatures original PSA amendment.
2. The amendment will be routed through the University enterprise contract system for approvals, posting (if required), and filing with state.
3. CCU shall send an executed original amendment to the PSC.

**VI. Signature Authorization**

The current limitations established by the University of Illinois Board of Trustees as executed by the SAVP required for authorization of University funds will be followed to approve amendments and field directives.

**VII. Illinois Public Higher Education Procurement Bulletin Posting**

In accordance with the Illinois Procurement Code (Section 15-25(b)), and the Procurement Rules for Higher Education (Section 526.3005) the Higher Education Chief Procurement Officer is responsible for publishing amendments/contract change orders and the respective required information in the Illinois Procurement Bulletin. The University Office of Capital Programs & Real Estate Services will post to the Illinois Public Higher Education Procurement Bulletin website (<http://www.procure.stateuniv.state.il.us>) all amendments/change orders greater than the Small Purchase Threshold, in accordance with agreement with the Procurement Policy Board and the Capital Development Board.

**VIII. University Office for Business and Financial Services (OBFS) Manual**

The University OBFS manual contains statements of policy and directives that guide University business practices, including but not limited to, information relating to the approval of financial documents.

**IX. Flowchart - See attached Visio Flowchart for Change Order Process**

**X. Forms –See Exhibit 1 and 2 for examples of those forms which can be found on the UOCP&RES website at: <http://www.uocpres.uillinois.edu/>**

*Change Order Form (Single)*

*Emergency Work Authorization/Field Directive Form (Single)*

*Change Order Form (Multiple)*

*Emergency Work Authorization/Field Directive Form (Multiple)*

*Field Directive for PSC*


**XI. Reporting**

A Change Order and Amendment Report showing the Project, Change Order, Amendment, and dollar value, shall be compiled quarterly by the UOCP&RES using data in FCPWeb , Kahua or other reporting software.


**Any questions regarding this policy shall be directed to:**

University of Illinois Office of Capital Programs & Real Estate Services  
807 South Wright Street, Suite 340, Champaign, Illinois, 61820, 217-333-5688

# Change Order (CO) Policy Workflow [Emergency Work Authorization (EWA)/Field Directive (FD)/Change Order (CO)]

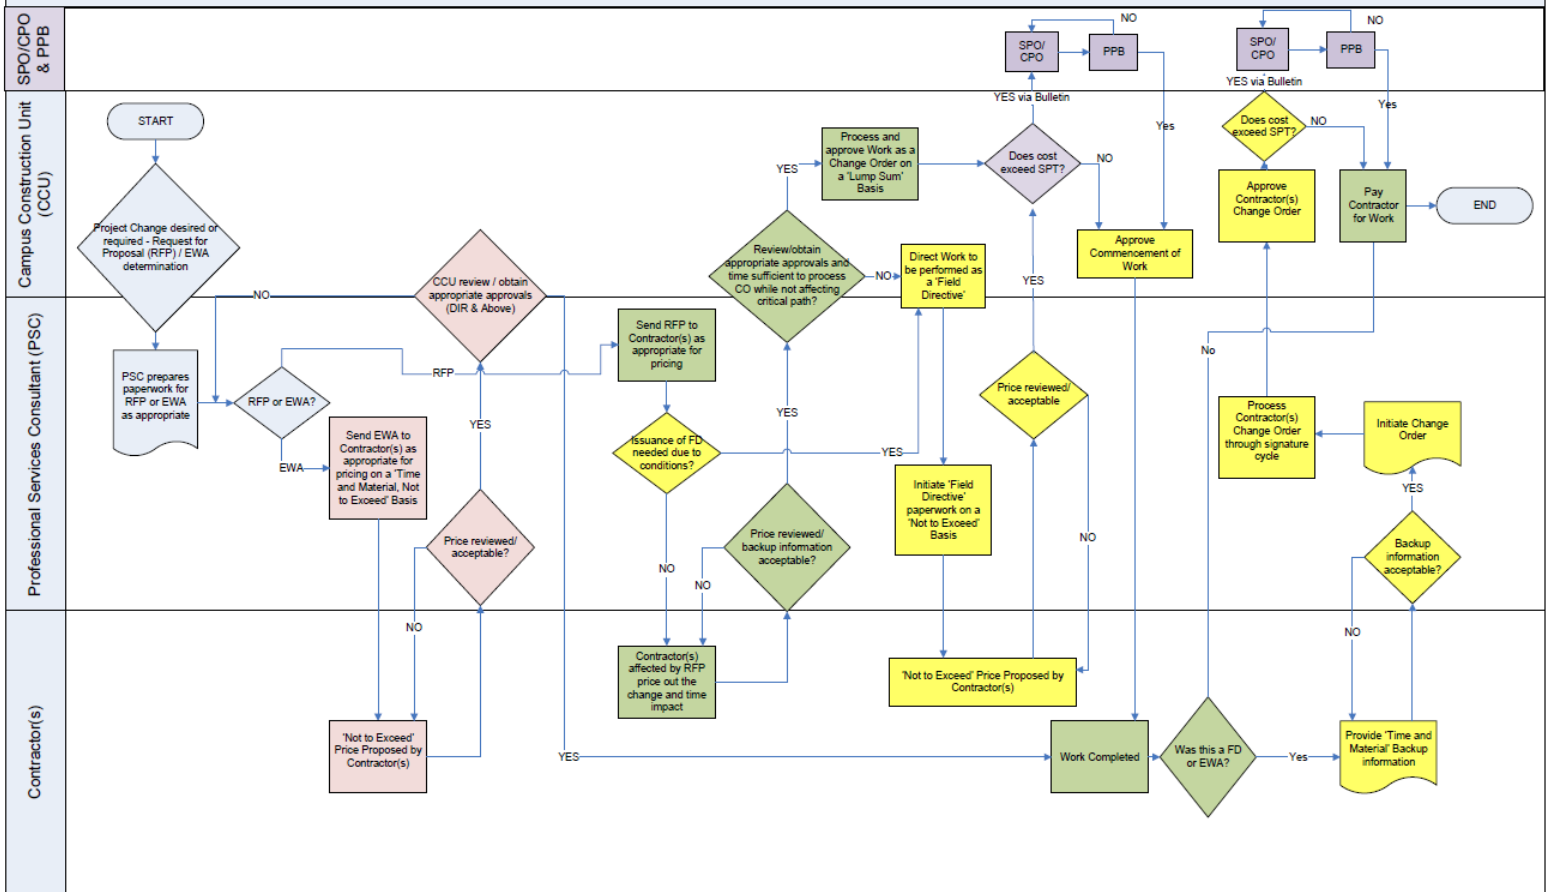

**PSC Field Directive (PSC FD) & Associated Amendment Process:** SYSTEMS Legend: P=PRZM F=FCPWeb K=Kahua C=C+ B=Banner File Last Updated: 11/6/2024

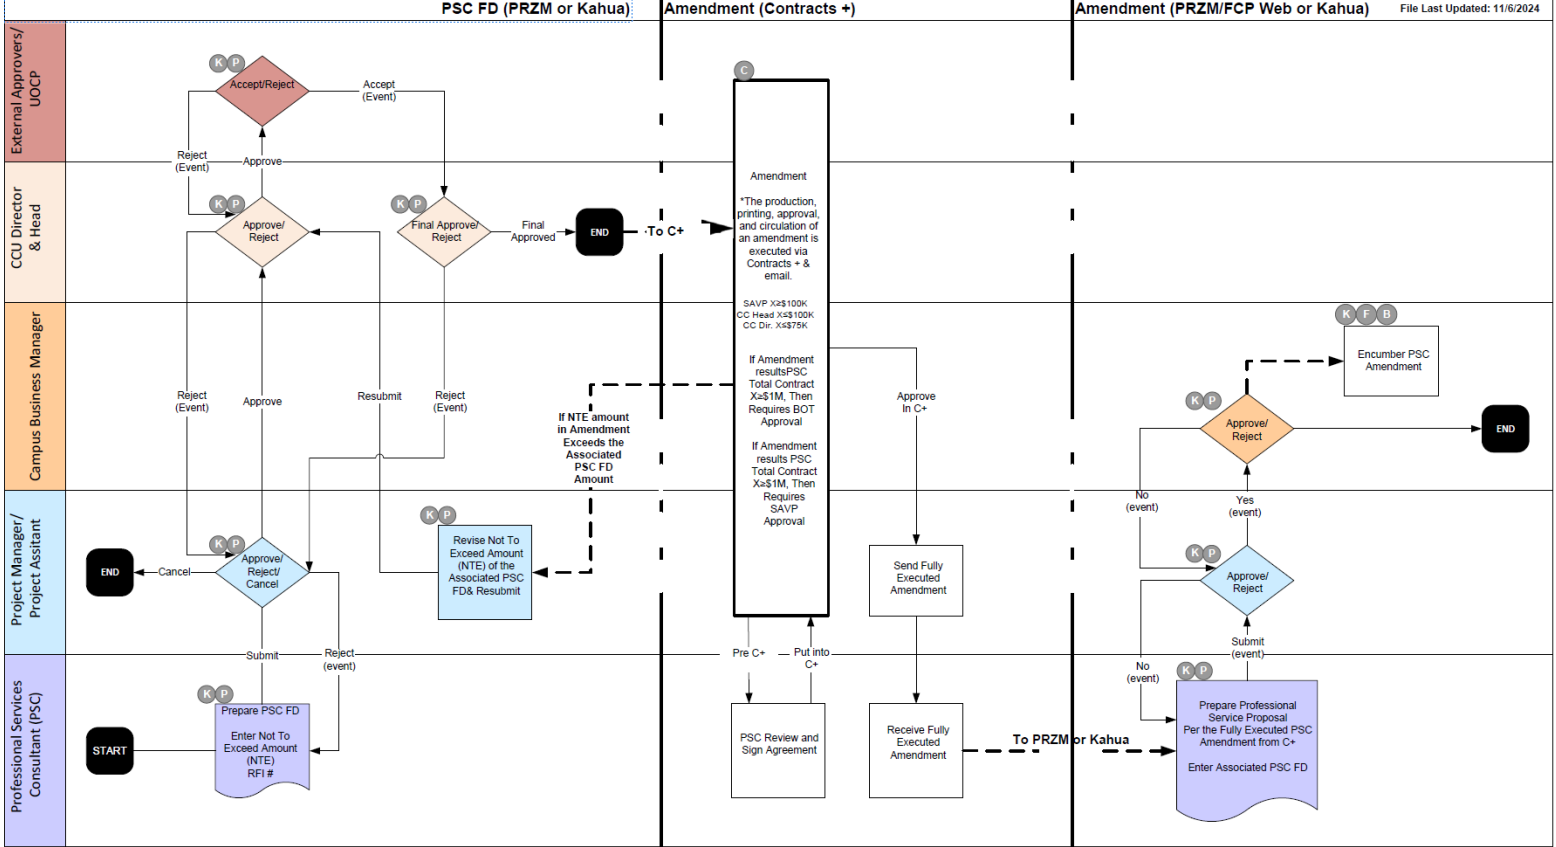

# Exhibit 1 - Page 1

## Construction Contract Change Order – Single (SAMPLE)

**UNIVERSITY OF ILLINOIS**  
**CONSTRUCTION CONTRACT CHANGE ORDER for**  
 • **Contractor (no assignment)**

UI Change Order No. \_\_\_\_\_  
 UI RFP/EWA No. \_\_\_\_\_  
 Change Order Amount \_\_\_\_\_  
 UI Document No. \_\_\_\_\_  
 UI Encumbrance No. \_\_\_\_\_

Project Name \_\_\_\_\_  
 Contractor Name/ Address \_\_\_\_\_  
 PSC Project No. \_\_\_\_\_

UI Project No. \_\_\_\_\_  
 Division of Work \_\_\_\_\_  
 Contractor Project No. \_\_\_\_\_

The above referenced contract is hereby amended to provide for the following described change(s) upon the terms set forth below:

Contractor shall provide: (SCOPE)

<b>Original Calendar Days to Complete the Work</b>	_____	<b>Original Contract Amount</b>	\$ _____
<b>Increase/(Decrease) in Calendar Days by Previous Change Orders</b>	_____	<b>Total of Previous Change Order(s)</b>	\$ _____
<b>Increase/(Decrease) in Calendar Days by this Change Order</b>	_____	<b>Increase/(Decrease) by this Change Order</b>	\$ _____
<b>Current Calendar Days to Complete the Work</b>	_____	<b>Revised Contract Amount</b>	\$ _____
<b>Revised Substantial Completion Date</b>	_ / _ / _____		

*As changed hereinabove, the above referenced contract shall continue in full force and effect.*

<b>CLASSIFICATION (for UI use only)</b>						<b>BUDGET/SCOPE (for UI use only)</b>	
Client Request		PSC Error	CM Error	Code/Std	Unforeseen Conditions	Does NOT affect project budget and/or scope	
Staff Changes/Scope		PSC Omission	CM Omission	Delivery/Schedule	Closeout		

Chart *	Fund *	Organization *	Account *	Program *	Activity	Location

**THE UNDERSIGNED HEREBY CERTIFY THAT THIS CONTRACT CHANGE ORDER IS GERMANE TO THE ORIGINAL CONTRACT AS SIGNED AND THAT THE CIRCUMSTANCES NECESSITATING THIS CONTRACT CHANGE ORDER WERE NOT REASONABLY FORESEEABLE AT THE TIME THE CONTRACT WAS SIGNED. THIS CONTRACT CHANGE ORDER IS IN THE BEST INTEREST OF THE UNIVERSITY OF ILLINOIS AND IS AUTHORIZED BY LAW.**

**PSC/CM/Contractor Approvals**

**University of Illinois Approvals**

Contractor \_\_\_\_\_ Date \_\_\_\_\_  
 Construction Manager (CM) (if applicable) \_\_\_\_\_ Date \_\_\_\_\_  
 Professional Services Consultant (PSC) \_\_\_\_\_ Date \_\_\_\_\_

Campus \_\_\_\_\_ Date \_\_\_\_\_  
 Board of Trustees of the University of Illinois–Interim Comptroller,  
 Paul Ellinger

Document Source: *Template No Changes*

Contract Type: *Capital*

Contract Sub Type: *Construction*

Form approved by Legal Counsel - UOCP&RES 07/18

**Exhibit 1 – Page 2  
EWA/FD – Single (SAMPLE)**

DATE

PROJECT TITLE

EMERGENCY WORK AUTHORIZATION (EWA) (No. \_\_\_\_\_)

FIELD DIRECTIVE (FD) (REFERENCE RFP # \_\_\_\_\_)

**Reason for Urgency**

**Description of Problem:**

**Action to be Taken:**

**Total “Not to Exceed” Cost to Complete** (Labor, Material, Mark up, etc.):

*Minimum information to be included in this section: Costs shall not exceed \$AMOUNT without prior written authorization by the Owner. Work to be invoiced on an hourly basis with daily time records submitted to the Contractor and Professional Services Consultant for approval. Time and Material backup information required for full payment at completion of Work.*

**Work Completion Required By:** \_\_\_\_\_ **Date** \_\_\_\_\_.

**Remarks:**

Recommended by: \_\_\_\_\_  
CONTRACTOR (Name, Firm and Division(s) of Work)

Reviewed by: \_\_\_\_\_  
PSC (scope & estimated cost(s) reviewed)

Reviewed by: \_\_\_\_\_  
CM (scope & estimated cost(s) reviewed)

Reviewed by: \_\_\_\_\_  
PM (scope & estimated cost(s) reviewed)

Approved by: \_\_\_\_\_  
DIRECTOR or above for all EWA's (CCU/UOCP&RES)  
PROJECT MANAGER or above per approval authority  
for Field Directives.

pm/sec

c: Professional Services Consultant  
Construction Manager (if applicable)  
Contractor(s)  
Project File

# EXHIBIT 1 – PAGE 3

## Construction Contract Change Order – Multiple (SAMPLE)

UNIVERSITY OF ILLINOIS

**CONSTRUCTION CONTRACT CHANGE ORDER**

- Contractor with Assigned Subcontractor(s) (AS)
- Assigned Subcontractor(s) (AS)

UI Change Order No. \_\_\_\_\_  
 UI RFP/EWA No. \_\_\_\_\_  
 Change Order Amount \_\_\_\_\_  
 UI Document No. \_\_\_\_\_  
 UI Encumbrance No. \_\_\_\_\_  
 UI Project No. \_\_\_\_\_  
 Contractor/AS Project No. \_\_\_\_\_  
 PSC Project No. \_\_\_\_\_

Project \_\_\_\_\_  
 Contractor/AS/Address \_\_\_\_\_

The above referenced contract is hereby amended to provide for the following described change(s) upon the terms set forth below:

Contractor shall provide: (SCOPE)

Original Calendar Days to Complete the Work \_\_\_\_\_ Current Calendar Days to Complete the Work \_\_\_\_\_  
 Increase/(Decrease) in Calendar Days by Previous Change Orders \_\_\_\_\_ Revised Substantial Completion Date \_\_\_\_\_  
 Increase/(Decrease) in Calendar Days by this Change Order \_\_\_\_\_

	Column A		Column B		Column C		TOTAL A+B+C
Contractor's Original Base Bid + Accepted Alternate(s)	\$	Total of Previous Change Order(s)	\$	Increase/(Decrease) by this Change Order	\$	Contractor's Revised Base Bid + Accepted Alternate(s) + Change Orders	\$
		Total of Previous Change Order(s) Assignment Fee	\$	TOTAL AS(s) increase(s) by this change order x 0.05	\$	Contractor's Revised Change Order(s) Assignment Fee	\$
<b>Contractor's SUBTOTAL</b>	<b>\$</b>		<b>\$</b>		<b>\$</b>		<b>\$</b>
Plumbing AS Original Subcontract Sum	\$	Total of Previous Change Order(s)	\$	Increase/(Decrease) by this Change Order	\$	Revised Subcontract Sum	\$
Heating AS Original Subcontract Sum	\$	Total of Previous Change Order(s)	\$	Increase/(Decrease) by this Change Order	\$	Revised Subcontract Sum	\$
Ventilation AS Original Subcontract Sum	\$	Total of Previous Change Order(s)	\$	Increase/(Decrease) by this Change Order	\$	Revised Subcontract Sum	\$
Electrical AS Original Subcontract Sum	\$	Total of Previous Change Order(s)	\$	Increase/(Decrease) by this Change Order	\$	Revised Subcontract Sum	\$
Fire Protection AS Original Subcontract Sum	\$	Total of Previous Change Order(s)	\$	Increase/(Decrease) by this Change Order	\$	Revised Subcontract Sum	\$
_____ AS Original Subcontract Sum	\$	Total of Previous Change Order(s)	\$	Increase/(Decrease) by this Change Order	\$	Revised Subcontract Sum	\$
<b>GRAND TOTAL (Contractor's Original Contract Sum)</b>	<b>\$</b>	<b>GRAND TOTAL of Contractor's Previous Change Order(s)</b>	<b>\$</b>	<b>GRAND TOTAL of Contractor's Increase/(Decrease) by this Change Order</b>	<b>\$</b>	<b>GRAND TOTAL of Contractor's SUBTOTAL + Revised Subcontract Sum(s) ("Contractor's Revised Contract Sum")</b>	<b>\$</b>

*As changed hereinabove, the above referenced contract shall continue in full force and effect.*

CLASSIFICATION (for UI use only)						BUDGET/SCOPE (for UI use only)	
Client Request	PSC Error	CM Error	Code/Std	Unforeseen Conditions		Does NOT affect project budget and/or scope	
Staff Changes/Scope	PSC Omission	CM Omission	Delivery/Schedule	Closeout		Affects project budget and/or scope (see attached documentation)	

Chart *	Fund *	Organization *	Account *	Program *	Activity	Location

THE UNDERSIGNED HEREBY CERTIFY THAT THIS CONTRACT CHANGE ORDER IS GERMANE TO THE ORIGINAL CONTRACT AS SIGNED AND THAT THE CIRCUMSTANCES NECESSITATING THIS CONTRACT CHANGE ORDER WERE NOT REASONABLY FORESEEABLE AT THE TIME THE CONTRACT WAS SIGNED. THIS CONTRACT CHANGE ORDER IS IN THE BEST INTEREST OF THE UNIVERSITY OF ILLINOIS AND IS AUTHORIZED BY LAW.

**PSC/Contractor Approvals**

**University of Illinois Approvals**

Assigned Subcontractor (AS) \_\_\_\_\_ Date \_\_\_\_\_  
 Contractor \_\_\_\_\_ Date \_\_\_\_\_

Campus\* \_\_\_\_\_ Date \_\_\_\_\_  
 Board of Trustees of the University of Illinois – Interim Comptroller\*, Paul Ellinger

Professional Services Consultant (PSC)\*  
 \* Approvals only required for Contractor's Change Order

Document Source: Template No Changes

Contract Type: Capital

Contract Sub Type: Construction

**EXHIBIT 1 – Page 4**  
**EWA/FD – Multiple (SAMPLE)**

**DATE**

**PROJECT TITLE**

**EMERGENCY WORK AUTHORIZATION (EWA)** (No. \_\_\_\_\_)

**FIELD DIRECTIVE (FD)** (REFERENCE RFP # \_\_\_\_\_)

**Reason for Urgency:**

**Description of Problem:**

**Action to be Taken:**

**Total “Not to Exceed” Cost to Complete** (Labor, Material, Mark up, etc.):

*Minimum information to be included in this section: Costs shall not exceed \$AMOUNT without prior written authorization by the Owner. Work to be invoiced on an hourly basis with daily time records submitted to the Contractor and Professional Services Consultant for approval. Time and Material backup information required for full payment at completion of Work.*

**Work Completion Required By:** \_\_\_\_\_ **Date** \_\_\_\_\_.

**Remarks:**

Recommended by: \_\_\_\_\_  
CONTRACTOR (Name, Firm and Division(s) of Work)

Reviewed by: \_\_\_\_\_  
PSC (scope & estimated cost(s) reviewed)

Reviewed by: \_\_\_\_\_  
CM (scope & estimated cost(s) reviewed)

Reviewed by: \_\_\_\_\_  
PM (scope & estimated cost(s) reviewed)

Approved by: \_\_\_\_\_  
DIRECTOR or above for all EWA's (CCU/UOCP&RES)  
PROJECT MANAGER or above per approval authority  
for Field Directives.

pm/sec

c: Professional Services Consultant  
Construction Manager (if applicable)  
Contractor(s)  
Project File

**EXHIBIT 2 – Page 1  
FD for PSC (SAMPLE)**

Date

**PSC DESIGN FIELD DIRECTIVE FOR EXPEDITED DESIGN WORK**

**PROJECT TITLE**

**Reason for Urgency:**

**Description of Problem:**

**Action to be Taken:**

**Total “Not to Exceed” Cost to Complete (Labor, etc.):**

*Minimum information to be included in this section: Costs shall not exceed \$AMOUNT without prior written authorization by the Owner. Design work to be invoiced on an hourly basis with daily time records submitted to the Owner for approval. Time record backup information required for full payment at completion of design. THE UNDERSIGNED HEREBY CERTIFY THAT THIS DESIGN IS GERMANE TO THE ORIGINAL AGREEMENT AS SIGNED AND THAT THE CIRCUMSTANCES NECESSITATING THIS PSC DESIGN FIELD DIRECTIVE WAS NOT REASONABLY FORESEEABLE AT THE TIME THE AGREEMENT WAS SIGNED. THIS PSC DESIGN FIELD DIRECTIVE IS IN THE BEST INTEREST OF THE UNIVERSITY OF ILLINOIS AND IS AUTHORIZED BY LAW.*

**Design Completion Required By:** \_\_\_\_\_ Date \_\_\_\_\_.

**Remarks:**

Recommended by: \_\_\_\_\_  
PSC (scope & estimated cost(s) reviewed)

Reviewed by (if applicable): \_\_\_\_\_  
CM (scope reviewed)

Reviewed by: \_\_\_\_\_  
PM (scope & estimated cost(s) reviewed)

Reviewed by: \_\_\_\_\_  
CCU Director (scope & estimated cost(s) reviewed)

Approved by: \_\_\_\_\_  
AVP

pm/sec

c: Professional Services Consultant  
Construction Manager (if applicable)  
Project File
